


## Gibson House and Historical Collection: Implementation Timeline

Task	Project Start	Project End
Install shelving in the Collections Conservation Facility	June	June
Conduct review of the entire collection and relocate items to more appropriate storage or display locations.	June	Estimated Winter 2019
Move collection items out of West Barn to the onsite Collections Conservation Facility	July	July
Conduct construction on West Barn, ADA pathways, pergola, electrical fence, and Administration building.	August	September
Landscaping Repairs and final construction touch ups	October	October
YoloArts to move onsite	October	October
Programming and exhibitions to begin at Gibson House property	Estimated February 2019	Continuous

## Collections Review Timeline Map

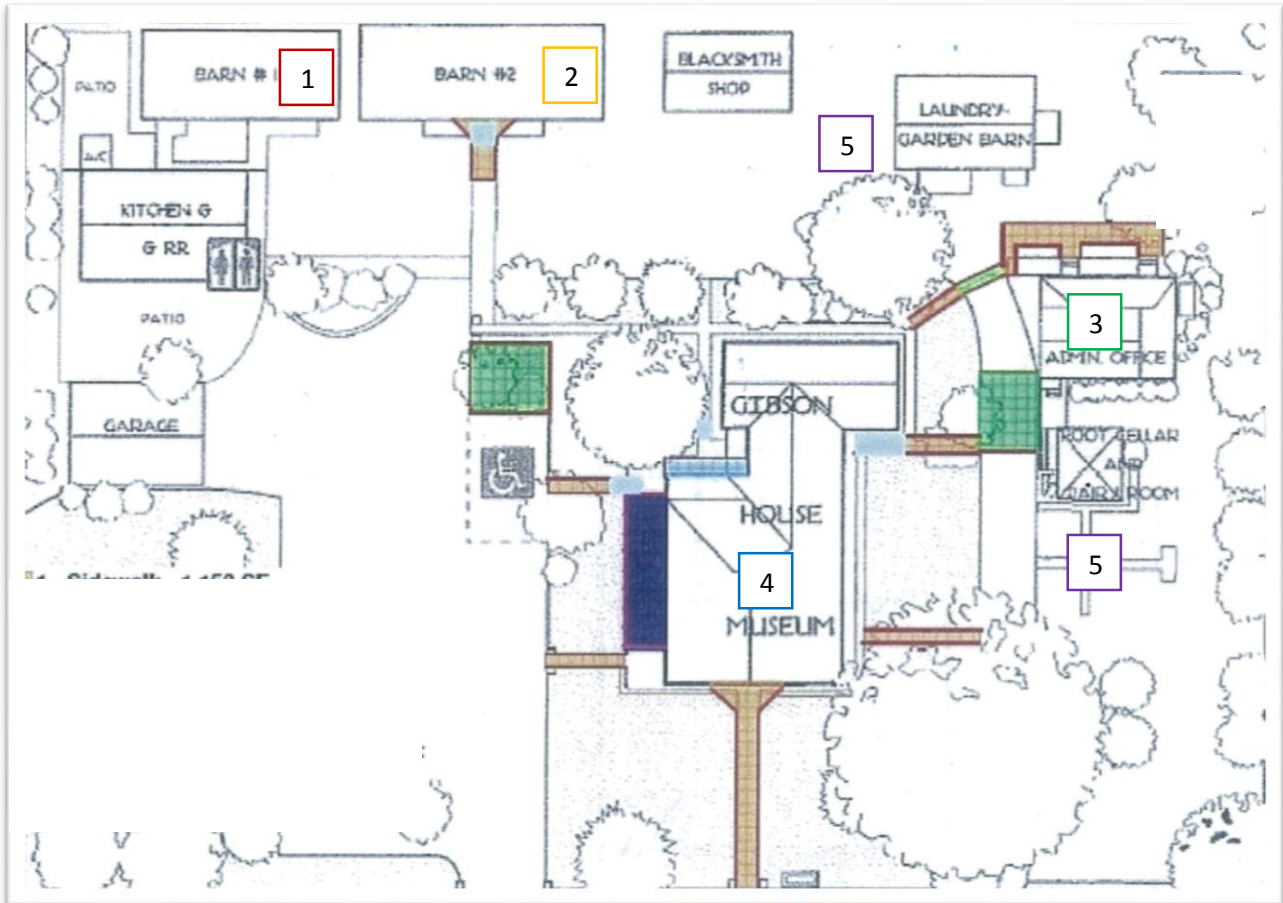

- 1 East Barn** – This location has YCHMs items used for events, tools, assorted items. Move the non-collection items out into a storage shed. *Proposed dates: July 3 – 6*
- 2 West Barn** – This location currently has the agricultural exhibit. These items will have to be moved to the collections conservation facility (former garage) to convert the barn to a multi-use classroom space. *Proposed dates: July 9 – August 3*
- 3 Administration** – This location has some collections items, collection documentation, and admin equipment that will have to be re-located to the collections and conservation facility (garage). *Proposed dates: August 6 - 31*
- 4 The House** – This location has collection items on the ground floor, second floor, and attic (as storage). The items in the attic will be a longer term project due to the volume. *Proposed dates: September 3 – November 30*
- 5 Outbuildings** – The dairy, root cellar, laundry, and blacksmith shop will all be re-configured and re-assessed for display and educational purposes. *Proposed dates: January 7 – March 29 2019*
