



Teichert Construction Woodland Office  
24207 County Road 100A  
Davis, CA 95616  
Phone: 530-406-4200 Fax: 530-406-4299

Job#: 11275.00 - Yolo County Airport Drainage Basin Improvements

# SUBMITTAL

Document No. 1 - Rev 0

10/16/2019

## County of Yolo

Yolo County Airport Drainage Basin Improvements  
County Rd. 95 & County Rd. 29  
Davis, CA

**ATTENTION: Gene Wais**

**SUBJECT:** CPM Progress Schedule

Per the table below enclosed and the attached documents are submittal items for review.

Please review and respond by: 11/05/2019

Item	Description	Rev	Date	Spec Section
1	CPM Progress Schedule	0	10/16/2019	GC - 3.01

**Comments:**



### ORIGINATED BY:

Company: Teichert Construction Woodland Office  
Contact: Armando Aguilar  
Title: Project Manager

Phone: 530-341-4282  
Fax: 530-406-4299  
Email: AAGUILAR@teichert.com

*Armando Aguilar*

Contact: Armando Aguilar  
Title: Project Manager

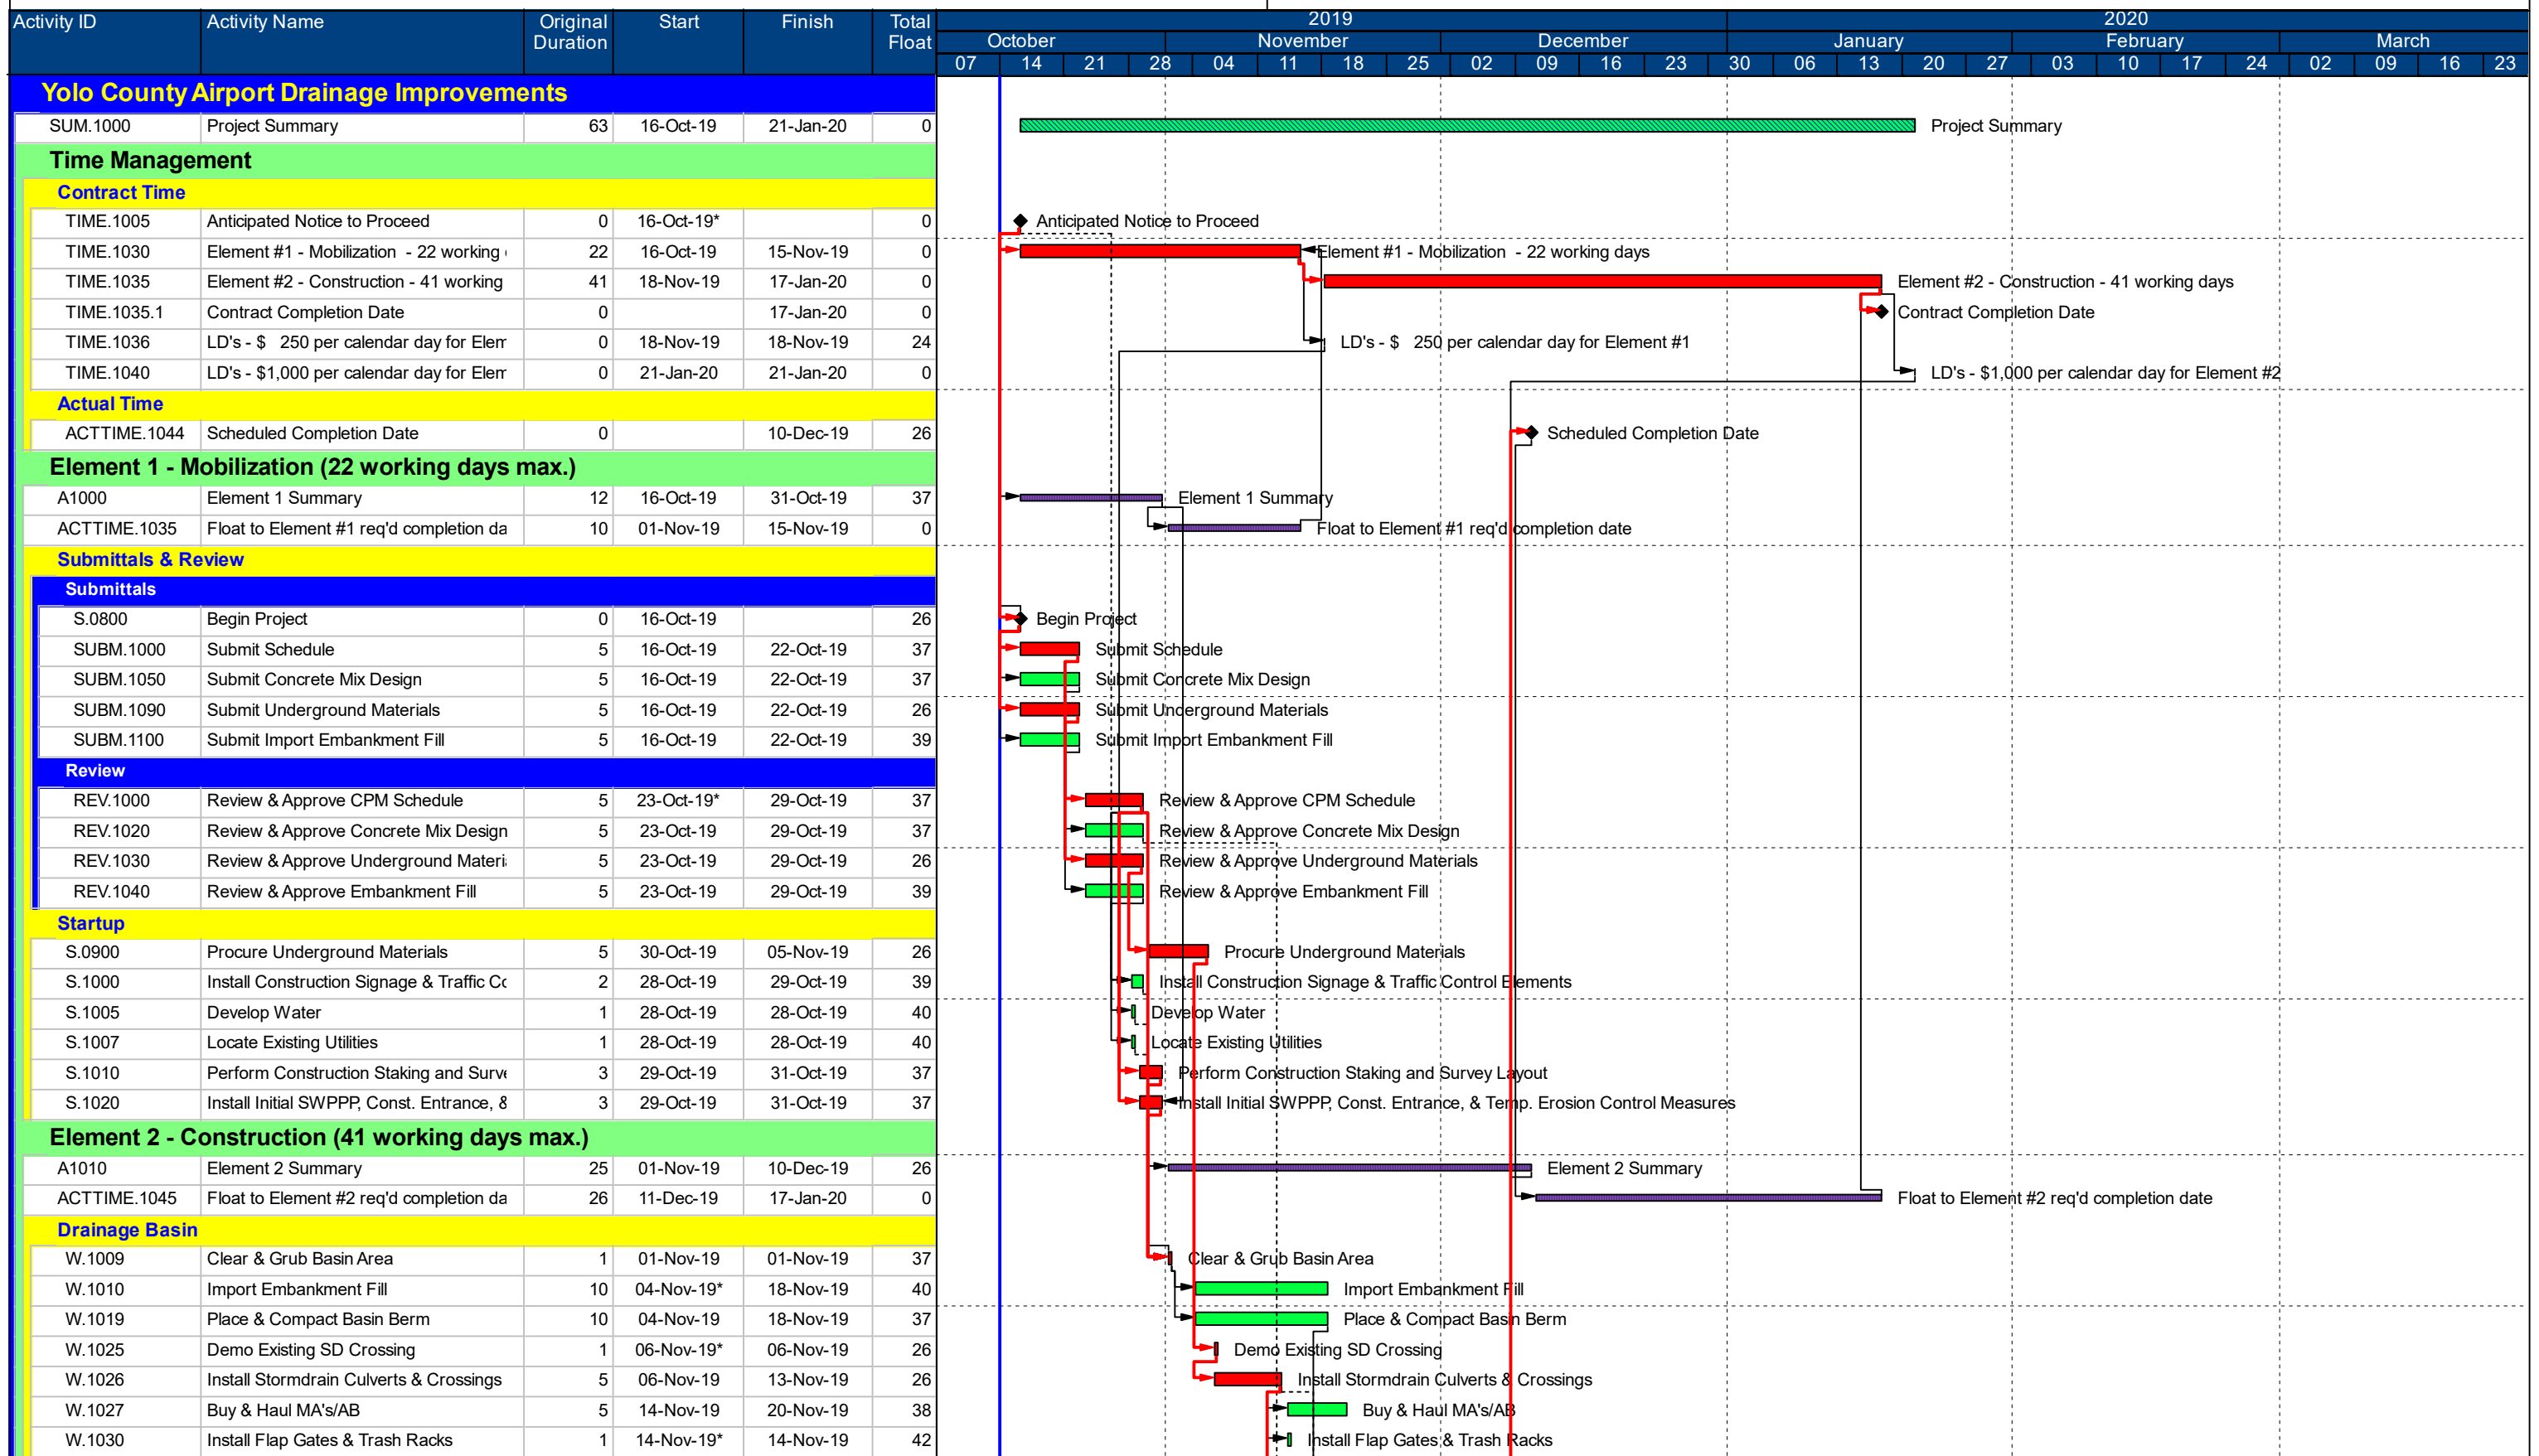

Activity ID	Activity Name	Original Duration	Start	Finish	Total Float	2019												2020								
						October				November				December				January			February			March		
						07	14	21	28	04	11	18	25	02	09	16	23	30	06	13	20	27	03	10	17	24
W.1031	Patch Pave SD Crossings	1	14-Nov-19*	14-Nov-19	42																					
W.1039	Subgrade, Place, Compact, & Finish AB	3	19-Nov-19*	21-Nov-19	37																					
W.1040	Trench Concrete Spillway Cutoff Walls	1	14-Nov-19*	14-Nov-19	26																					
W.1049	Form & Pour Concrete Spillway	7	15-Nov-19	25-Nov-19	26																					
W.1059	Place RSP	2	26-Nov-19	27-Nov-19	26																					
W.1069	Finish Grade / Prep for Hydroseed	2	02-Dec-19	03-Dec-19	26																					
W.1079	Place Permanent Erosion Control	4	04-Dec-19	09-Dec-19	26																					
W.1079.1	Allowance for Road Repair	1	10-Dec-19	10-Dec-19	26																					
W.1180	Punchlist/ Clean & Sell	1	10-Dec-19	10-Dec-19	26																					
W.1200	Job Completion	0		10-Dec-19	26																					

Remaining Level of Effort    
  Actual Work    
  Critical Remaining Work    
  WBS Summary  
 Actual Level of Effort    
  Remaining Work    
 ◆ ◆ Milestone
